PROJECT PLANING/SCHEDULE

Clients Name :

Project Name : Comprehensive development of Roads and Drains in Ward no 16 Rajarajeshwari Nagara Assembly Constituency Under PACKAGE - 2019-20-RRN-DIV(01)

Project Manager /Team Leader : Naveen
Project Start Date : 13-Jul-20
Project End Date : 13-Jul-21
Project Length in Days : 365

Sl. No	Assignment	Unit	Boq Qnty	Start Date	End Date	No. of Working Days
1	Removing & Refixing stone slabs of drains and pointing in C.M (1:3)complete as per the direction of Engineer in charge	Sqm	15544.40	14-Jul-20	16-Nov-20	125
2	Excavation for road, drains and similar works KSRRB 300-1. Earthwork excavation by manual means in ordinary soil	Cum	8482.26	24-Jul-20	26-Nov-20	125
3	Plain cement concrete 1:3:6 mix with crushed stone aggregate 40 m nominal size mechanically mixed, placed in foundation	Sqm	216.18	3-Aug-20	6-Dec-20	125
4	Providing and laying plain/reinforced cement concrete for side drains using M20 nominal mix concrete with OPC at 300	Cum	643.83	23-Aug-20	31-Dec-20	130
5	Providing T.M.T. steel reinforcement for R.C.C. work including straightening, cutting, bending, hooking, placing in	ton	40.23	13-Aug-20	16-Dec-20	125
6	Providing and constructing granite / trap / basalt size stone masonry in foundation with cement mortar, stone hammered	Cum	82.80	3-Aug-20	6-Dec-20	125
7	Providing and constructing precast concrete solid blocks with compressive strength not less than 3.5 Newton per sqm with	Sqm	6557.60	3-Aug-20	6-Dec-20	125
8	Providing ruled pointing to coursed stone masonry with cement mortar, 20mm deep, after raking joints to depth of	Sqm	22433.60	13-Aug-20	11-Dec-20	120
9	Providing and laying in position plain cement concrete of Mix 1:2:4 with OPC @ 240/kgs, with 20mm and down size graded	Cum	516.90	13-Aug-20	26-Dec-20	135
10	Providing and laying in position plain cement concrete of Mix 1:2:4 with OPC @ 240/kgs, with 20mm and down size graded	Cum	341.61	13-Aug-20	26-Dec-20	135
11	Providing & laying precast drain cover slab of 100 mm thickness in CM 1:3 including cost of all materials, labour,	Sqm	5053.31	17-Sep-20	14-Feb-21	150
12	Providing and Fixing RCC Precast Cover Slab of 250 mm Thick for Drains in Cement Concrete M-20 using graded	Sqm	157.00	2-Oct-20	10-Jan-21	100
13	Removing and resetting of kerb stones.complete as per the direction of Engineer in charge	Rmt	10058.25	14-Jul-20	16-Nov-20	125
14	Providing and fixing pre cast solid concrete kerb stones of size 450x150x500 mm made out of CC 1:2:4 and finished	m/s	11900.00	27-Sep-20	4-Feb-21	130
15	Painting two coats after filling the surface with synthetic enamel paint in approved shades on new plastered concrete	Sqm	6165.20	7-Oct-20	14-Feb-21	130
16	Construction of embankment with approved material Gravel/Murrum with all lifts and leads, transporting to site,	Cum	661.20	13-Aug-20	16-Dec-20	125
17	Providing and laying heavy duty cobble stones 75mm thick interlock pavers, using cement and course sand for	Sqm	2088.00	23-Aug-20	21-Dec-20	120
18	Excavation for roadwork in soil with hydraulic excavator of 0.90 cum bucket capacity including cutting and loading in	Cum	3559.55	26-Nov-20	5-Apr-21	130
19	Construction of granular sub-base Grading-V as Sub-base and drainage layer by providing coarse graded crushed stone	Cum	2466.80	6-Dec-20	5-Apr-21	120
20	Providing, laying, spreading and compacting crushed stone aggregates of granite / trap / basalt to wet mix macadam	Cum	2728.99	16-Dec-20	25-Apr-21	130
21	Providing and applying primer coat with S.S. bitumen emulsion on prepared surface of granular base such as WMM	Sqm	11865.18	26-Dec-20	5-May-21	130
22	Cleaning the existing black topped surface with brooms, soft brushes and finally dusting with old gunny bags and / or	Sqm	33955.92	5-Jan-21	20-May-21	135
23	Providing and applying tack coat using 80/100 grade bitumen(VG10) on the prepared black topped surfaces at 2.5	Sqm	89413.51	20-Jan-21	4-Jun-21	135
24	Providing and laying dense graded bituminous macadam using crushed aggregates of specified grading, premixed with VG30	Cum	2345.06	30-Jan-21	9-Jun-21	130
25	Providing and laying bituminous concrete using crushed aggregates of specified grading, premixed with bituminous	Cum	1876.04	9-Feb-21	29-Jun-21	140
26	Road Marking with Hot Applied Thermoplastic Compound with Reflectrising Glass Beads on Bituminous Surface:-	Sqm	2716.25	19-Feb-21	29-Jun-21	130
27	Providing and fixing of road stud 100x 100 mm, diecast in aluminium, resistant to corrosive effect of salt and grit, fitted	m/s	3142.00	1-Mar-21	12-Jul-21	133

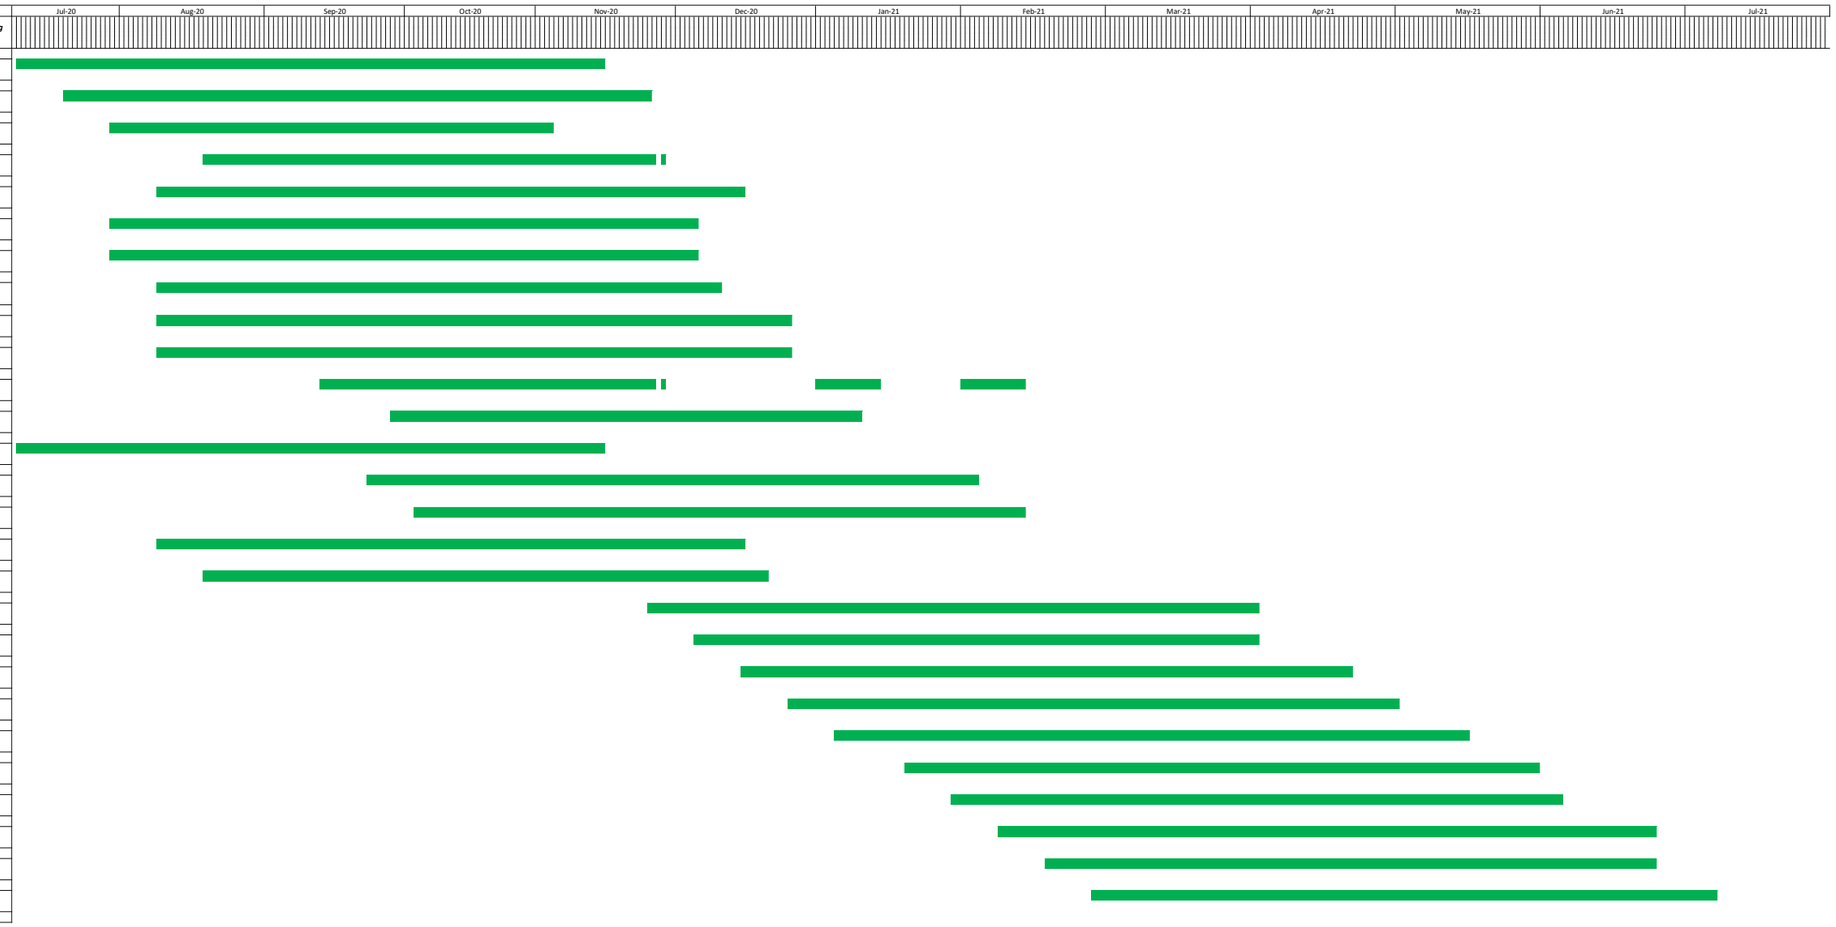

: Time Table For Work Complete
